

Work Order ID 149092

Tuesday, July 19, 2016 2:44:59 PM


149092

Page 1

Item ID: D4635-141 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Fwd Ceiling Replacement Panel Assembly, LH
Start Date: 7/13/2016 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 7/19/2016 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: DAS 21 Date: JUL 20 2016 Tooling: _____ Date: _____ Run Start ***NR1***
QC: 9-89 Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4635	F								
100		0.00							
100									
HandThermo	Memo	0.14							
Hand Finishing Thermoforming	Pick Kit								

  **AUG 12 2016**

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : ☐					

Work Order ID 149092

Tuesday, July 19, 2016 2:44:59 PM

149092

Page 2

Item ID: D4635-141 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Fwd Ceiling Replacement Panel Assembly, LH
Start Date: 7/13/2016 Start Qty: 1.00 ***1*** Cust Item ID:
Required Date: 7/19/2016 Req'd Qty: 1.00 ***1*** Customer:
Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
110		0.01							
110									
Small Fab									
Small Fab									
	Memo	0.19							
	Assemble as per Dwg D4635-141								
	Bond foam core to inside of panel								
	3M Scotch Weld 1300 Batch: <u>M13S436</u>								
	1- Scuff bonding surface to eliminate in-perfections and increase bonding and clean with wash& wipe								
	2- Locate and glue down Channel Assy, angles, brackets, and mounting pads using 3M Plastic welder II.(see note 8)								
	Batch # <u>M13S436</u>								
	Expiry Date <u>03/11/2017</u>								
	3- Apply labels as per Dwg. and seal with 3M 3950 edge sealer(see note 9)								
	Batch: <u>M13S435</u>								
120	QC5- Inspect part completeness to step on W/O	0.00							
120									
QC									
Quality Control	Memo	0.00							

DAS
9
9-89

⑦ 16-08-16

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition			
				Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐			
OTHER : _____					

1 49092

Tuesday, July 19, 2016 2:44:59 PM

N900040100

Setup Start *NS1*

Stop ***NS2***

Start Date: 7/13/2016 **Start Qty:** 1.00 ***1***

Required Date: 7/19/2016 **Req'd Qty:** 1.00 *** 1 ***

Reference:

Run Start *NR1*

Stop *NR2*

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

130

Identify as per dwg & Stock Location:_____ 0.00

130

Packaging

Memo

PPP 149129 0.00

Packaging

DAS
27

9-89

AUG 16 2016

140

QC21- Final Inspection - Work Order Release	0.00
---	------

140

QC

Memo

Quality Control

0.02

**DAS
21
9-89**

AUG 18 2016

DAS
21
9-69

AUG 17 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

Picklist Print

Tuesday, July 19, 2016 2:44:59 PM

Page 1

Work Order ID: 149092

149092

Parent Item: D4635-141

D4635-141

Parent Item Name: Fwd Ceiling Replacement Panel Assembly, LH

Start Date: 7/13/2016

Required Date: 7/19/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP Rev. A 12/08/09 New Issue DL
 12/11/08 Doc Release DL
 Update13/07/09 DL verf:DD
 13/12/09 DL
 Ipp Rev. E Dwg Update 14/01/09 DL
 Dwg. Update 15/01/27 DL

IPP Rev B
 IPP Rev. C Dwg.
 IPP Rev D Dwg Update
 IPP Rev. F

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D5022-1		Manufactured	No			100	Each	19.0000	1	1			
D5022-1									**				
Foam, Side Panel, Fwd													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				MF010				19					
				123925				9					
				126184				10					
D4635-1		Manufactured	No			100	Each	0.0000	1	1			
D4635-1									**				
Fwd Ceiling Panel, LH													
D4695-041		Manufactured	No			100	Each	7.0000	1	1			
D4695-041									**				
Channel Assembly, LH													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				ST446				7					
				125011				3					
				129263				4					
D4669-1		Manufactured	No			100	Each	44.0000	2	2			
D4669-1									**				
Bracket													
				<u>Location</u>				<u>Loc Qty</u>		<u>Loc Code</u>			
				MF004				44					
				124100				4					
				125017				40					

AUG 12 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐								
Misidentified ☐	Past Due ☐	OTHER :							

Picklist Print

Tuesday, July 19, 2016 2:44:59 PM

Page 2

Work Order ID: 149092

149092

Parent Item: D4635-141

D4635-141

Parent Item Name: Fwd Ceiling Replacement Panel Assembly, LH

Start Date: 7/13/2016

Required Date: 7/19/2016

Start Qty: 1.00

Required Qty: 1.00

D4732-5 Manufactured No

100 Each 14.0000 1 1

D4732-5

Label

PC

<u>Location</u>	<u>Loc Qty</u>	<u>Loc Code</u>
MF005	14	
<u>120062</u>	3	
123202	11	

D4732-9 Manufactured No

100 Each 13.0000 1 1

D4732-9

Label

PC

<u>Location</u>	<u>Loc Qty</u>	<u>Loc Code</u>
MF005	13	
<u>120065</u>	1	
123204	12	

D4732-29 Manufactured No

100 Each 13.0000 1 1

D4732-29

Label

PC

<u>Location</u>	<u>Loc Qty</u>	<u>Loc Code</u>
MF005	13	
120075	1	
<u>123214</u>	12	

D4732-33 Manufactured No

100 Each 13.0000 1 1

D4732-33

Label

PC

AUG 12 2016

<u>Location</u>	<u>Loc Qty</u>	<u>Loc Code</u>
MF005	13	
<u>120077</u>	1	
123216	12	

Tuesday, July 19, 2016 2:44:59 PM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																											
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval																																																								
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																							
Root Cause		FAULT CATEGORY																																																													
Environment ☐	Design ☐	Doc/Data ☐	Equip/Tooling ☐	Handling/Pre ☐	Material ☐	Internal Transport ☐	Tribal Knowledge ☐	LOA ☐	Substation ☐	Past Expiry Date ☐	Misidentified ☐	No Re-verification ☐	Operator ☐	Offset/Setup ☐	Supplier ☐	Training ☐	Use for Testing ☐	Poor Information ☐	Rushing ☐	Product Improvement ☐	Process Improvement ☐	Manufacturing Process ☐	Past Due ☐	Pressure/Forced ☐	Bending ☐	Centre Not Concentric ☐	Cracks ☐	Crimp/Kink/Ripple/Wave ☐	Cuffs ☐	Crushing ☐	Heat Treat ☐	Wave/Twist in Tube ☐	Marks/Chatter ☐	Temperature/Cure ☐	Set-up ☐	BOM/Route ☐	Broken/Damage/Defect ☐	Inspection Incomplete/Unqualified ☐	Contamination ☐	Countersink ☐	Cut Too Short ☐	Instructions Incomplete/Unclear ☐	Drill Holes ☐	Power Loss/Surge ☐	Folio/Program ☐	Grain ☐	Weld ☐	Wrong Stock Pulled ☐	Out of Sequence ☐	Off-set ☐	Mislabeled ☐	Fit/Function ☐	Misaligned/off center ☐	Positioned Wrong ☐	Outside Dimensions ☐	Over/Under tolerance ☐	Part Incorrect ☐	Part Lost/Missing ☐	Part Moved ☐	Drawing ☐	Finish ☐	Misread ☐	Turning Sequence ☐
																								OTHER :																																							

Picklist Print

Page 3

Tuesday, July 19, 2016 2:44:59 PM

Work Order ID: 149092

149092

Parent Item: D4635-141

D4635-141

Parent Item Name: Fwd Ceiling Replacement Panel Assembly, LH

Start Date: 7/13/2016

Required Date: 7/19/2016

Start Qty: 1.00

Required Qty: 1.00

MPNY-750S-9-C

Purchased

No

100

Each

851.0000

7

7

MPNY-750S-9-C

PC

Mounting Pad

Location

Loc Qty

Loc Code

ST583

851

M130423

851

7

AUG 12 2016

Tuesday, July 19, 2016 2:44:59 PM

Shop Packet Print

Page 3

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
						QC / QA Coordinator Approval			


Root Cause			FAULT CATEGORY																																																												
Environment ☐	Design ☐	Doc/Data ☐	Equip/Tooling ☐	Handling/Pre ☐	Material ☐	Internal Transport ☐	Tribal Knowledge ☐	LOA ☐	Substation ☐	Past Expiry Date ☐	Misidentified ☐	No Re-verification ☐	Operator ☐	Offset/Setup ☐	Supplier ☐	Training ☐	Use for Testing ☐	Poor Information ☐	Rushing ☐	Product Improvement ☐	Process Improvement ☐	Manufacturing Process ☐	Past Due ☐	Pressure/Forced ☐	Bending ☐	Centre Not Concentric ☐	Cracks ☐	Crimp/Kink/Ripple/Wave ☐	Cuffs ☐	Crushing ☐	Heat Treat ☐	Wave/Twist in Tube ☐	Marks/Chatter ☐	Temperature/Cure ☐	Set-up ☐	BOM/Route ☐	Broken/Damage/Defect ☐	Inspection Incomplete/Unqualified ☐	Contamination ☐	Countersink ☐	Cut Too Short ☐	Instructions Incomplete/Unclear ☐	Drill Holes ☐	Power Loss/Surge ☐	Folio/Program ☐	Grain ☐	Weld ☐	Wrong Stock Pulled ☐	Out of Sequence ☐	Off-set ☐	Mislabeled ☐	Fit/Function ☐	Misaligned/off center ☐	Positioned Wrong ☐	Outside Dimensions ☐	Over/Under tolerance ☐	Part Incorrect ☐	Part Lost/Missing ☐	Part Moved ☐	Drawing ☐	Finish ☐	Misread ☐	Turning Sequence ☐
OTHER : _____																																																															

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT

WITHOUT NOTICE
WORK ORDER

NO. 149092 *MCJ*
16-07-20

ITEM	QTY	P/N	DESCRIPTION
1	X	D4635-141	LH, FWD CEILING REPLACEMENT PANEL ASSY
2	1	D4635-1	LH, FWD CEILING PANEL
3	2	D4669-1	BRACKET
4	1	D4695-041	LH CHANNEL ASSEMBLY
5	1	D4732-5	LABEL
6	1	D4732-9	LABEL
7	1	D4732-29	LABEL
8	1	D4732-33	LABEL
9	1	D5022-1	FOAM, SIDE PANEL, FWD
10	7	MPNY-750S-9-C	MOUNTING PAD

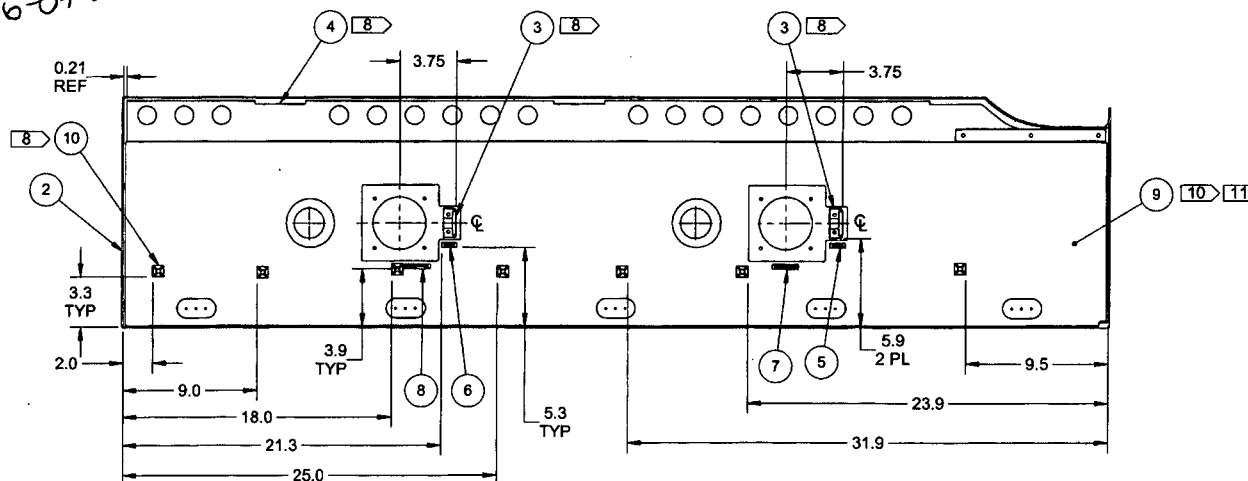

D4635-141 LH, FWD CEILING REPLACEMENT PANEL ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: N/A
- 8) APPLY A BEAD (0.20 TO 0.30 WIDE) OF DEVCON PLASTIC WELDER II (0.25 INSIDE OF BOTH EDGES OF PART) TO BOND D4669-1, D4695-041 & MPNY-750S-9C. WAIT FOR 2 TO 4 HOURS FOR FUNCTIONAL CURE
- 9) LOCATE LABELS AS SHOWN, SEAL LABELS USING 3950 EDGE SEALER OVER LABEL TOP SURFACE
- 10) APPLY AN EVEN COAT OF 3M SCOTCH WELD 1300L CONTACT ADHESIVE TO BOND D5022-1 FOAM CORE TO INSIDE OF PANEL
- 11) CENTER D5022-1 FOAM ON D4635-1

RELEASED

2015 JAN 26 *up*

APPROVED

DESIGN	RF	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	RF		
CHECKED	AK	DRAWING NO.	REV. F
MFG. APPR.	DL	D4635	SHEET 9 OF 18
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	OUTBOARD CEILING PANELS	NTS
DATE	14.11.28	COPYRIGHT © 2012 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR LOANED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
